



**Heron Resources Limited
Tarago Operations Pty Limited**

Woodlawn Mine

SML 20

Summary of Environmental Monitoring Data

Environmental Protection Licence Number 20821

Project Approval 07_0143MOD2

Record Update – 30 June 2019



Table of Contents

1. Introduction	1
1.1 Introduction	1
1.2 Explanation of units of measurement	2
1.3 Abbreviations	2
2. Meteorological Monitoring	3
3. Air Quality Monitoring	6
3.1 Depositional Dust	6
3.2 Atmospheric dust – particulate matter	8
4. Noise Monitoring	13
5. Blasting	14
6. Complaints	17
Appendix A – Historical deposition dust record	18
Appendix B – Daily weather statistics –	19
April 2019	19

Figures

Figure 1. Prevailing wind direction (percentage for month) February – April 2019	5
Figure 2. Monthly dust deposition gauge results	7
Figure 3. Annual rolling average for insoluble solids (g/m ² /month)	8
Figure 4. PM ₁₀ and TSP raw data results	11
Figure 5. PM₁₀ and TSP annual rolling average results	11

Tables

Table 1. Licence information	1
Table 2. Supporting information of EPL monitoring requirements.....	2
Table 3. Summary of weather conditions for previous 3 months (February – April 2019)	3
Table 4. Depositional dust (g/m ² /month - insoluble solids) recorded since May 2017	6
Table 5. Deposited dust limits	8
Table 6. Background deposited dust values for Woodlawn (Jan 2015 – Sep 2017).....	8
Table 7. Average deposited dust values since commencement of construction (Sep 2017 – Feb 2019)	8
Table 8. Raw results for PM ₁₀ and TSP.....	9
Table 9. TSP and PM ₁₀ limits	12
Table 10. Noise criteria (dB(A))	13
Table 11. Monitoring locations for noise monitoring.....	13
Table 12. EPL & Project Approval limits for airblast and ground vibration.....	14

Table 13. Blast Monitoring Results	Error! Bookmark not defined.
Table 14. Blast monitoring April 2019	14
Table 15. Complaints register.....	17

1. Introduction

1.1 Introduction

Tarago Operations Pty Ltd, a wholly owned subsidiary of Heron Resources Limited, holds Environment Protection Licence 20821 (EPL 20821) issued by the Environment Protection Agency (EPA) under the Protection of the Environment operations Act 1997 (the Act) and operates under the conditions of Project Approval 07_0143MOD2 granted by the NSW Department of Planning and Infrastructure for the Woodlawn Mine Project. This report has been prepared to satisfy the reporting requirements of the Act as directed by the EPA and also for Condition 11, Schedule 6 of the Project Approval.

This report summarises environmental monitoring results for the Woodlawn Mine for the period 1 – 30 June 2019. Historical depositional dust results recorded by Veolia since January 2015 are included in Appendix A to this report to provide a background air quality baseline.

A summary of the EPL information is provided in the following tables. Table 1 shows the licence information and Table 2 summarises the frequency and units for monitoring data for the reporting period. The EPL was subject to variation on 18 Jan 2019. Links to the previous version and the 18 January 2019 version are in [Table 1](#).

Table 1. Licence information

Environment Protection Licence number	20821
Licensee	Tarago Operations Pty Ltd
Licensee address	Level 7, Suite 702 191 Clarence Street SYDNEY NSW 2000
Premises	Woodlawn Mine Project 507 Collector Road TARAGO NSW 2580
Link to full licence on the EPA website	http://app.epa.nsw.gov.au/prpoeoapp/ViewPOEOLicence.aspx?DOCID=115339&SYSUID=1&LICID=20821 https://apps.epa.nsw.gov.au/prpoeoapp/ViewPOEOLicence.aspx?DOCID=155570&SYSUID=1&LICID=20821
Link to Notice of Variation of EPA licence	http://app.epa.nsw.gov.au/prpoeoapp/ViewPOEONotice.aspx?DOCID=-1&SYSUID=1&LICID=20821 https://apps.epa.nsw.gov.au/prpoeoapp/ViewPOEONotice.aspx?DOCID=-1&SYSUID=1&LICID=1572566
Complaints Telephone Number	Sydney Office (02) 9119 8111 Woodlawn Office (02) 9119 8140

Table 2. Supporting information of EPL monitoring requirements

Parameter	Monitoring site	Monitoring frequency	Unit of measure
Air quality monitoring: Deposited Dust (insoluble solids)	DG 22*, DG28*, DG33* DG34	Monthly	g/m ² /month
TSP	HVAS-1	24 hours every six days	µg/m ³
PM10	HVAS-2	24 hours every six days	µg/m ³

*Monitoring undertaken by Veolia

1.2 Explanation of units of measurement

- **mg/m³** = milligrams per cubic metre
- **g/m²/month** = grams per square metre per month
- **µg/m³** = micrograms per cubic metre
- **Day** = 7am to 6pm Monday to Saturday and 8am to 6pm Sunday and public holidays
- **Evening** = 6pm to 10pm on any day
- **Night** = 10pm to 7am Monday to Saturday and 10pm to 8am Sunday and public holidays

1.3 Abbreviations

- TOP – Tarago Operations

2. Meteorological Monitoring


Heron is required to undertake meteorological monitoring on site. Veolia operate an approved weather station (EPA licence 11436, Point 9). As weather may influence monitoring results for dust and noise a summary showing the rainfall, temperature, evaporation and average wind speed for the three months April to June 2019 is summarised in Table 3. The detailed March daily weather data is shown in Appendix B.

Seasonal conditions continue to be dry, with April recording no rainfall, and both May and June below average. Soil moisture deficiencies continue. The autumn vegetation growth flush did not occur due to continued low rainfall so ground cover remains sparse. The ongoing dry weather has continued and the plant growth index is extremely low. Likewise, the soil water index is extremely low. The NSW DPI have reported that the southeast region remains in 'drought'. The combined drought indicator conditions for Werriwa Parish at 30 June 2019 indicated the site remained in drought (Source: <https://www.dpi.nsw.gov.au/climate-and-emergencies/droughthub/information-and-resources/seasonal-conditions/ssu/nsw-state-seasonal-update-june-2019>)

Table 3. Summary of weather conditions for previous 3 months (April – Jun 2019)

	April	May	June
Total rainfall (mm)	0	31.5	48
Total number of wet days	0	10	11
Average maximum temperature at 2m (°C)	19.9	14.3	11.8
Average minimum temperature at 2m (°C)	9.2	5.8	3.5
Average wind speed at 10m (m/s)	2.73	3.61	2.57
Evapotranspiration (mm)	81.1	52.7	31.4

The prevailing wind direction trends for the 3 months April - June 2019 is displayed in Figure 1 using wind roses. The wind roses depict the wind speed and direction recorded at 10 m above ground level. During the period the winds were variable from east and west in April but was predominantly from the west during May and June. Evapotranspiration was below rainfall in June, but minimally and therefore preventing any improvement to the severe soil moisture deficit following several months of extremely dry conditions.

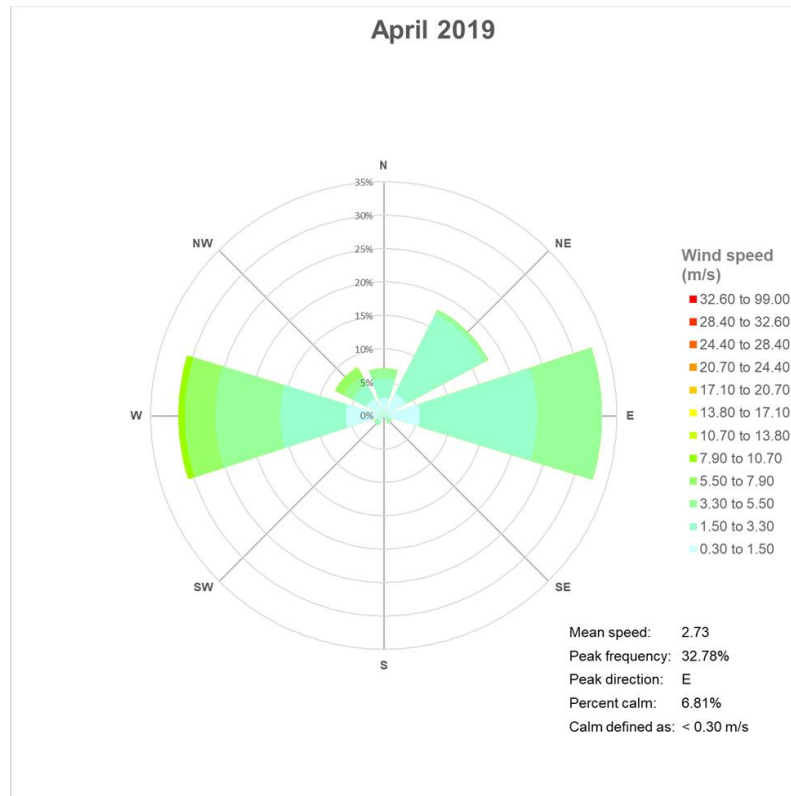

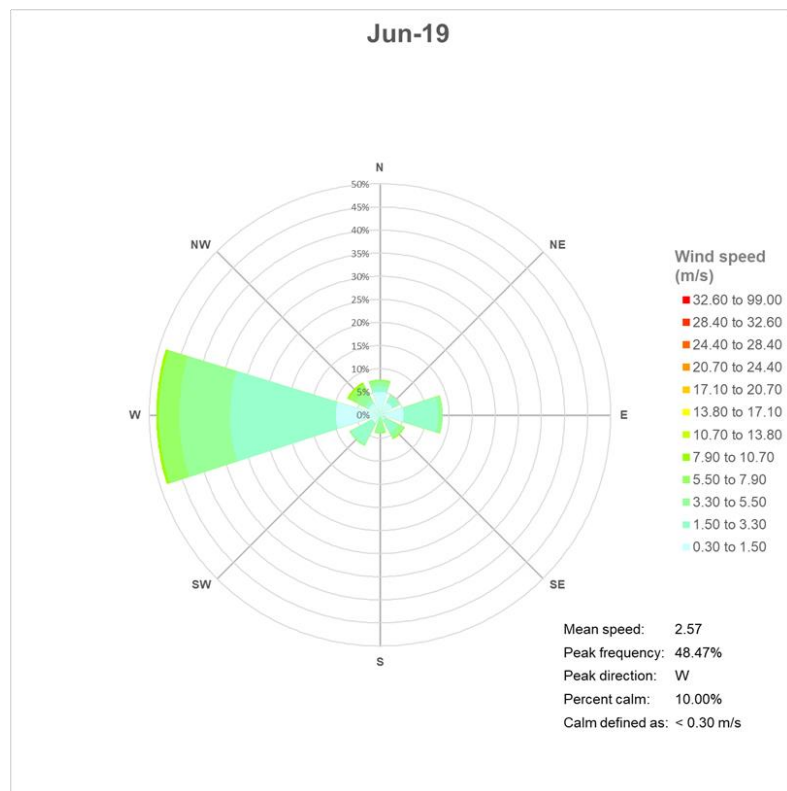
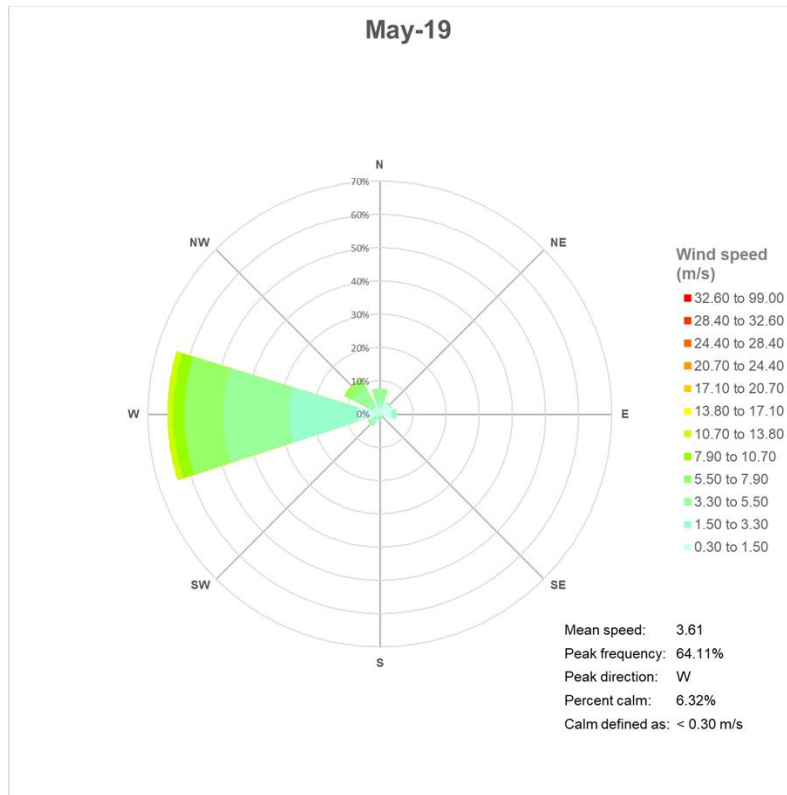


Figure 1. Prevailing wind direction (percentage for month) April – June 2019

3. Air Quality Monitoring

The Air quality monitoring results for Woodlawn Mine are summarised in the following sections.

3.1 Depositional Dust

Depositional dust monitoring around the Woodlawn site is undertaken on a monthly basis. Four depositional dust gauges DG22, DG28, DG33 and DG34 are present to monitor the levels of depositional dust. They are located on Site as follows:

- DG22 – East side of void
- DG28 – Pylara
- DG33 – MBT plant
- DG34 – Behind core shed

DG24, has been used to record dust to the west of the void. Due to construction of the box cut and mine office infrastructure for the new mine the gauge was decommissioned on 31 Jan 2018. The Veolia EPL has been varied accordingly. A new dust gauge, DG34, was installed on 1 Feb 2018. The gauge is still positioned west of the void, but in a new location.

Historical monthly raw results for the period January 2015 – Mar 2017 are shown in Appendix A – Historical deposition dust record. The results were recorded by Veolia prior to the issue of Heron’s EPL and are presented to provide an indication of the background air prior to commencement of the TOP construction.

The EPA licence for the Woodlawn Mine project was issued on May 2017. The raw results for depositional dust commencing May 2017 are recorded in Table 4.

Table 4. Depositional dust (g/m²/month - insoluble solids) recorded since May 2017

Date sampled	DG22	DG24	DG28	DG33	DG34
May 2017	3.3	0.6	0.8	<0.2	
Jun 2017	1.4	0.4	<0.2	<0.2	
Jul 2017	1.7	0.5	2.4	<0.2	
Aug 2017	3.7	0.5	4.0	0.2	
Sep 2017	4.8	0.8	2.1	0.4	
Oct 2017	3.9	3.0	1.0	0.5	
Nov 2017	5.2	1.9	0.8	0.4	
Dec 2017	2.4	1.9	0.4	0.9	
Jan 2018	5.3	4.7	1.8	1	
Feb 2018	2.4	Decommissioned	1.1	1.4	2.8
Mar 2018	3.7		0.4	1.4	0.7
Apr 2018	8.6		2.7	2.4	1.3
May 2018	1.8		1.6	0.3	1
Jun 2018	1.6		3.2	<0.2	0.2
Jul 2018	0.7		1.1	0.3	<0.2
Aug 2018	4.1		6.6	0.9	1.0
Sep 2018	2.3		1.3	0.2	0.6

Oct 2018	5.5		2.7	1.3	2.2
Nov 2018	7.3		3.8	2	12.6
Dec 2018	4.2		8	2.3	8.4
Jan 2019	6.4		8.8	4.2	9.7
Feb 2019	8		8.4	3.4	11.2
Mar 2019	5.6		8.0	2.3	2
Apr 2019	5.3		0.9	0.2	0.4
May 2019	4.3		3.0	1.8	2.1

A graphical representation of raw depositional dust gauge monitoring results from January 2015 until end of May 2019 is shown in Figure 2.

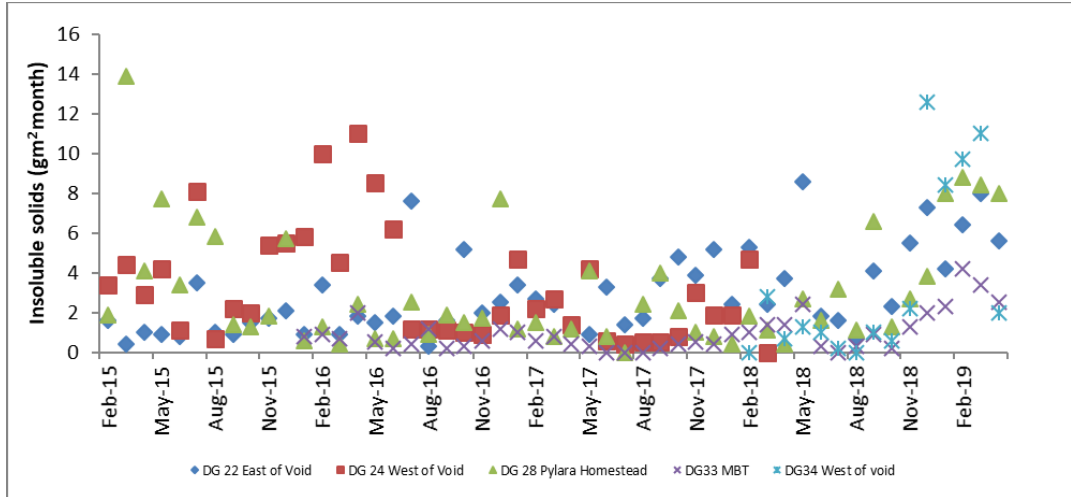


Figure 2. Monthly dust deposition gauge results

Figure 3 shows the annual rolling average for deposited dust (insoluble solids grams per m² per month) for the four monitoring sites between Jul 2016 and end May 2019.

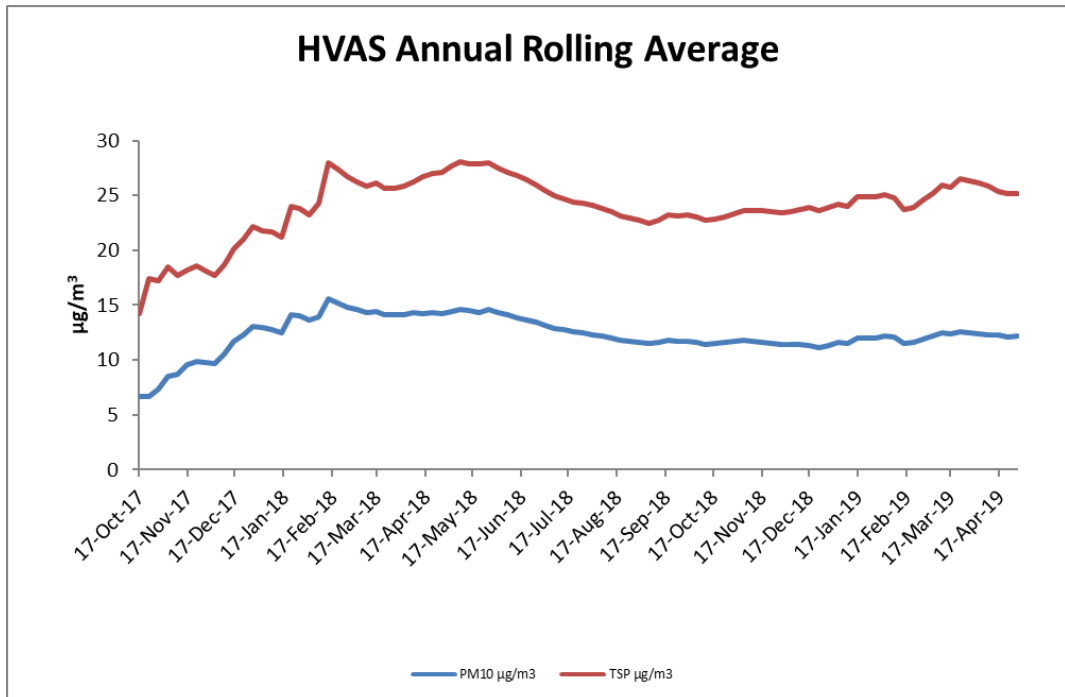


Figure 3. Annual rolling average for insoluble solids (g/m²/month)

The limits for deposited dust are outlined in the Project Approval. The limits are detailed in Table 5.

Table 5. Deposited dust limits

Pollutant	Averaging period	Maximum increase in deposited dust level	Maximum total deposited dust level
^c Deposited dust	Annual	^b 2 g/m ² /month	^a 4 g/m ² /month

- ^a Total impact (i.e. Incremental increase in concentrations due to the project plus background concentrations due to all other sources).
- ^b Incremental impact (i.e. incremental increase in concentrations due to the project on its own)
- ^c Deposited dust is to be assessed as insoluble solids as defined by Standards Australia, AS/NZS 3580.10.1:2003: Methods for Sampling and Analysis of Ambient Air – Determination of Particulate Matter – Deposited Matter – Gravimetric Method.

Data recorded prior to 14 Sep 2017 is detailed in Appendix A and summarised in Table 6 to show the average background deposited dust levels recorded prior to commencement of construction. The data shows that the annual rolling average for all four depositional dust gauges did not exceed 4 g/m²/month during the period Jan 2015 to Sep 2017 nor increase the background by more than 2 g/m²/month.

Table 6. Background deposited dust values for Woodlawn (Jan 2015 – Sep 2017)

	DG22	DG24	DG28	DG33
Individual gauge background average	2.1	3.5	3.0	0.7
Overall background average	2.5			

Average raw deposited dust levels from each gauge for the period since construction commenced (Sep 2017 to May 2019) is shown in Table 7. DG24 was decommissioned on 31 Jan 2018 and DG34 was commissioned on 1 Feb 2018.

Table 7. Average deposited dust values since commencement of construction (Sep 2017 – Apr 2019)

	DG22	DG24	DG28	DG33	DG34
Individual gauge average	4.4	Decommissioned	3.3	1.4	3.6
Overall average	3.1				

3.2 Atmospheric dust – particulate matter

The Project Approval requires monitoring of total suspended particulate (TSP) matter and particulate matter < 10µm (PM₁₀) to ensure particulate matter emissions generated by the project do not exceed the criteria listed at any residence on privately owned land. High volume air sampling (HVAS) equipment for atmospheric monitoring was installed on 16 October 2017 at Pylara, the nearest residence located to the east of Woodlawn Mine. Monitoring commenced on 17 October 2017 and is undertaken for a 24 hour cycle every 6 days.

Raw results obtained from the HVAS for PM₁₀ and TSP are shown in Table 8 and Figure 4. The rolling 12 month average is shown in Figure 5.

Table 8. Raw results for PM₁₀ and TSP

Date start of 24 hour sampling run (7:00am – 7:00am)	PM ₁₀ µg/m ³	TSP µg/m ³
17 Oct 2017	6.7	14.2
23 Oct 2017	6.7	20.6
29 Oct 2017	8.6	16.8
4 Nov 2017	12.0	22.3
10 Nov 2017	9.5	14.4
16 Nov 2017	13.9	20.6
22 Nov 2017	11.8	20.9
28 Nov 2017	9.1	15.0
4 Dec 2017	8.4	14.5
10 Dec 2017	18.3	27.1
16 Dec 2017	23.7	35.5
22 Dec 2017	18.6	30.4
28 Dec 2017	22.3	35.5
3 Jan 2018	11.9	17.3
9 Jan 2018	9.5	20.1
15 Jan 2018	8.7	14.2
21 Jan 2018	40.6	69.2
27 Jan 2018	11.4	19.7
2 Feb 18	7.4	13.2
8 Feb 18	19.1	44
14 Feb 18	48.3	102
20 Feb 18	7.3	15.5
26 Feb 18	7.1	10.7
4 Mar 18	8.9	15.9
10 Mar 18	9.2	17.7
16 Mar 18	14.9	31.9
22 Mar 18	6.7	14.4
28 Mar 18	14.9	25.5
3 Apr 18	15	30.1
9 Apr 18	18.5	38.4
15 Apr 18	12.0	42.2
21 Apr 18	18.0	34.1
27 Apr 18	11.6	29.5
3 May 18	19.8	47.5
9 May 18	22.4	40.7
15 May 18	10.1	21.3
21 May 18	8.0	27
27 May 18	24.1	31.9
2 Jun 18	2.7	9.0
8 Jun 18	5.7	12.8
14 Jun 18	4.9	15.8
20 Jun 18	6.6	11.9
26 Jun 18	2.7	4.6
2 Jul 18	6.2	16.8
8 Jul 18	<1.0	3.7
14 Jul 18	5	8.4

20 Jul 18	4.5	14.8
26 Jul 18	6.2	16.8
1 Aug 18	7.1	13.8
7 Aug 18	4.9	9.8
13 Aug 18	3.1	8.7
19 Aug 18	2.6	7.0
25 Aug 18	5.5	10.3
31 Aug 18	7.9	12.9
6 Sep 18	3.6	7.7
12 Sep 18	17.9	39.7
18 Sep 18	22.1	49.5
24 Sep 18	5.8	16.8
30 Sep 18	11.8	27.5
6 Oct 18	6.3	14.8
12 Oct 18	3.6	6.3
18 Oct 18	6.9	16.0
24 Oct 18	15.4	34.3
30 Oct 18	15.4	34.3
5-Nov-18	15.5	38.4
11-Nov-18	7.2	17.7
17-Nov-18	6.1	19.4
23-Nov-18	5.1	14.4
29-Nov-18	6.6	9.9
5-Dec-18	8.5	18
11-Dec-18	16.4	39
17-Dec-18	19.7	47.7
23-Dec-18	3.8	13.4
29-Dec-18	33.5	51.7
4-Jan-19	29.9	37
10-Jan-19	4.4	8.5
16-Jan-19	40	65.7
22-Jan-19	39.5	69.8
28-Jan-19	9.1	17.6
3-Feb-19	23.1	30.3
9-Feb-19	10.5	23.7
15-Feb-19	15.6	37.5
21-Feb-19	12.1	24.9
27-Feb-19	25.4	53.9
5 Mar 19	25.4	53.9
11 Mar 19	26.5	61.8
17 Mar 19	6	19.8
23 Mar 19	22.3	60.6
29 Mar 19	9.8	17.8
4 Apr 19	7.9	13.2
10 Apr 19	11.3	22.5
16 Apr 19	10.8	15.7
22 Apr 19	8.2	17.7
28 Apr 19	14.5	34.7

4 May 19	2.4	8.1
10 May 19	3.9	7.8
16 May 19	7.3	16.2
22 May 19	7.9	18.3
28 May 19	5.5	22.1

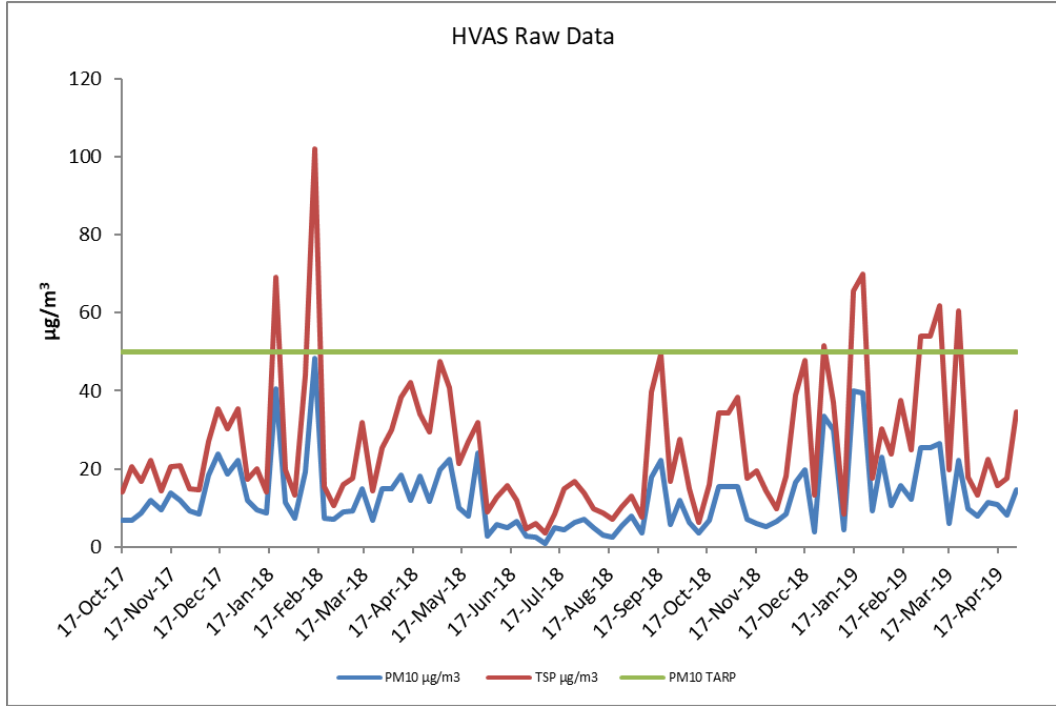


Figure 4. PM₁₀ and TSP raw data results

Annual rolling average results for both PM₁₀ and TSP are shown in Figure 5.

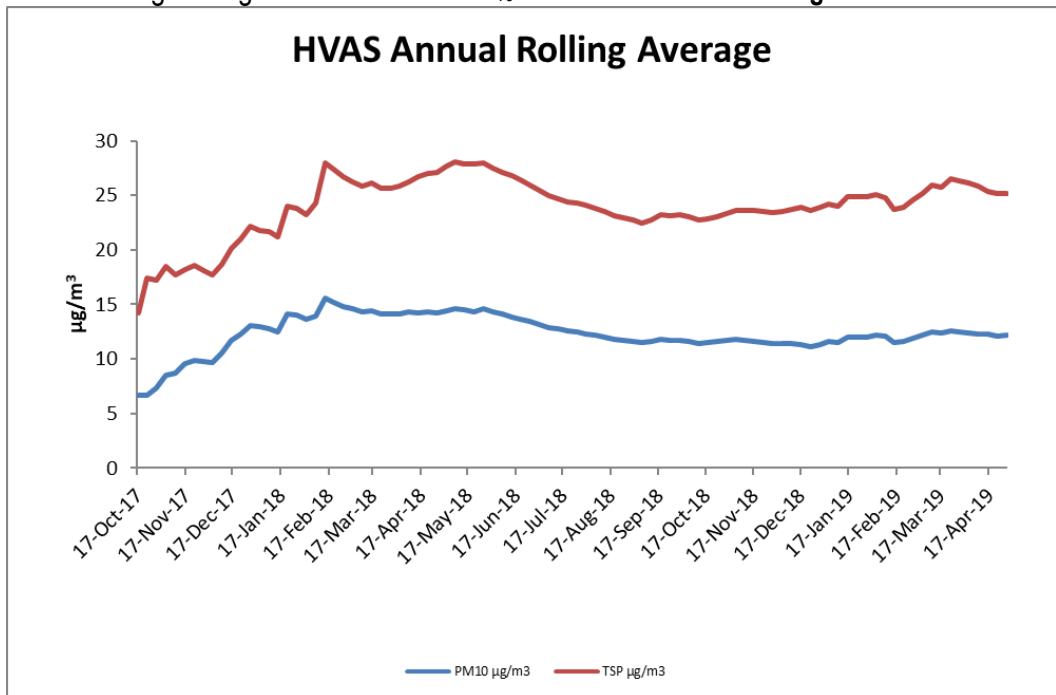


Figure 5. PM₁₀ and TSP annual rolling average results

The limits for TSP and PM₁₀ are outlined in the Project Approval. The limits are detailed in Table 9.

Table 9. TSP and PM₁₀ limits

Pollutant	Averaging Period	^dCriterion
Total suspended particulate (TSP) matter	Annual	^a 90 µg/m ³
Particulate matter < 10 µm (PM ₁₀)	Annual	^a 30 µg/m ³
Particulate matter < 10 µm	24 hour	^a 50 µg/m ³

- ^a Total impact (i.e. Incremental increase in concentrations due to the project plus background concentrations due to all other sources).
- ^d Excludes extraordinary events such as bushfires, prescribed burning, dust storms, fog, fire incidents or any other activity agreed by the Director-General.

Compliance summary:

The PM₁₀ and TSP results for 24 hour period are within the criteria set out in the PA.

The annual average emissions are within the criteria set out in the PA with the PM₁₀ annual average concentration up to 31 May 2019 of 11.2µg/m³ and TSP of 23.6 µg/m³.

4. Noise Monitoring

The noise criteria to be met at any residence on privately owned land is contained in the project approval and described in Table 10.

The EPL requires that the premises must not emit noise exceeding an L_{Aeq} , 15 minute noise level of 35 dB(A) at any sensitive receivers during the operational phase. There are no specified limits covering the construction phase however the Interim Construction Noise Guideline allows for construction activities being undertaken during daytime to be 10 dB(A) above background.

The meteorological conditions to be met during noise monitoring include:

- a) Wind speeds up to 3 m/s at 10 m above ground level; or
- b) Temperature inversion conditions of up to 3°C/100m and wind speeds up to 2 m/s at 10m above ground level

Table 10. Noise criteria (dB(A))

Receivers	Day/Evening/Night ($L_{Aeq}(15\text{minute})$)	Night ($L_{A1(\text{max})}$)
All residential receivers	35	45

Attended noise surveys were unable to be carried out due to wind exceeding the speed criteria for noise monitoring.

Table 11. Monitoring locations for noise monitoring

Monitoring location	Description
NM1	Pylara - Residence owned by Veolia
NM2	Cowley Hills – Residence owned by Veolia
NM3	Woodlawn – Residence owned by Veolia

Attended noise measurements were undertaken using a calibrated Type 1, Castle Group Ltd dBAir environmental monitor. Noise monitoring was carried out on 6 and 21 Jun 2019 using two measurement profiles as follows:

- Measurement 1 – Frequency weighting A, time weighting F
- Measurement 2 – Frequency weighting C, time weighting F.

Real time meteorological conditions were obtained at each location using a BL-300 Anemo-thermometer and hygrometer and validated using the authorised Woodlawn on-site weather station. Readings are routinely taken at the Pylara, Woodlawn and the Cowley Hills residences. All locations represent the nearest receptors and are owned by Veolia. The results show that the construction activities have little noise impact on any of the receptor locations.

Compliance statement: The construction program complies with the nominated construction noise guidelines.

5. Blasting

Airblast overpressure and the ground vibration level are required to be monitored for all blasts undertaken during operations. EPL and Project Approval limits at any residence on privately owned land are detailed in Table 12.

Table 12. EPL & Project Approval limits for airblast and ground vibration

Time of blasting	Airblast overpressure (dB(Lin Peak))	Ground vibration (mm/s)	Allowable exceedance
Any time	120	10	0%
Day	115	5	5% of the total number of blasts over a period of 12 months
Evening	-	2	5% of the total number of blasts over a period of 12 months
Night, and all day on Sundays and public holidays	-	1	0%

Blast monitoring was conducted continuously for on-site monitoring during the period 1-30 June 2019. No off-site monitoring was conducted during this period. Given the results of on-site recording it is unlikely that any exceedances off site could have been experienced during the period. The timing of blast events during the period 1-30 June are shown in Table 13.

Table 13. Blast monitoring June 2019

Date	Time	PA Exceedance	Mic Peak (dBL)	Peak Vector Sum 1 (mm/s)
1 Jun 2019	0645			
1 Jun 19	0930			
1 Jun 19	1830			
2 Jun 19	0645			
3 Jun 19	0645			
3 Jun 19	1830			
4 Jun 19	0645			
5 Jun 19	0530			
5 Jun 19	1830			
6 Jun 19	0640			
6 Jun 19	1920			
7 Jun 19	0630			
7 Jun 19	1830			
8 Jun 19	1845			
9 Jun 19	0630			
10 Jun 19	0630			

10 Jun 19	1845			
10 Jun 19	2330			
11 Jun 19	Nil			
12 Jun 19	0600			
12 Jun 19	1830			
13 Jun 19	0645			
13 Jun 19	2030			
14 Jun 19	0620			
15 Jun 19	0630			
15 Jun 19	1830			
16 Jun 19	0620			
16 Jun 19	1830			
17 Jun 19	0630			
17 Jun 19	1830			
17 Jun 19	2230			
18 Jun 19	0630			
19 Jun 19	0530			
19 Jun 19	1830			
20 Jun 19	0630			
20 Jun 19	1845			
21 Jun 19	0600			
22 Jun 19	0600			
22 Jun 19	1630			
22 Jun 19	1845			
23 Jun 19	0630			
23 Jun 19	1445			
24 Jun 19	0315			
24 Jun 19	1230			
25 Jun 19	0130			
25 Jun 19	1820			
26 Jun 19	0130			
26 Jun 19	1550			
27 Jun 19	0235			
27 Jun 19	0630			
27 Jun 19	1410			

On 28 Jun 19 the monitor was relocated to Pylara for off-site monitoring.

Date	Time	PA Exceedance	Mic Peak (dBL)	Peak Vector Sum 1 (mm/s)
28 Jun 19	0115	Nil trigger		
28 Jun 19	0630	Nil trigger		
28 Jun 19	1000	Nil trigger		
28 Jun 19	1530	Nil trigger		
28 Jun 19	2300	Nil trigger		
29 Jun 19	0630	Nil trigger		

29 Jun 19	1830	Nil trigger		
29 Jun 19	2200	Nil trigger		
30 Jun 19	0030	Nil trigger		
30 Jun 19	0630	Nil trigger		
30 Jun 19	1305	Nil trigger		
30 Jun 19	2030	Nil trigger		

Compliance statement: Airblast overpressure and ground vibration monitoring results during blasting operations have remained below the project limits.

6. Complaints

No complaints occurred during the reporting period.

Table 14. Complaints register

Date and time	Complainant	Nature of complaint	Recorded by	Corrective action	Date closed

Appendix A – Historical deposition dust record

Date sampled	DG22	DG24	DG28	DG33
Jan 2015	1.6	3.4	1.9	
Feb 2015	0.4	4.4	13.9	
Mar 2015	1.0	2.9	4.1	
Apr 2015	0.9	4.2	7.7	
May 2015	0.8	1.1	3.4	
Jun 2015	3.5	8.1	6.8	
Jul 2015	1.0	0.7	5.8	
Aug 2015	0.9	2.2	1.4	
Sep- 2015	1.5	2.0	1.3	
Oct 2015	1.7	5.4	1.8	
Nov 2015	2.1	5.5	5.7	
Dec 2015	0.9	5.8	0.6	0.8
Jan 2016	3.4	10	1.3	0.9
Feb 2016	0.9	4.5	0.4	0.7
Mar 2016	1.8	11	2.4	2.0
Apr 2016	1.5	8.5	0.7	0.5
May 2016	1.8	6.2	0.7	0.2
Jun 2016	7.6	1.2	2.5	0.4
Jul 2016	1.2	0.3	23	1.2
Aug 2016	1.1	0.6	1.9	0.2
Sep 2016	1.0	1.2	6.0	0.3
Oct 2016	0.9	2.0	3.2	0.6
Nov 2016	1.9	2.2	2.6	1.2
Dec 2016	4.7	1.1	1.7	1.0
Jan 2017	2.2	2.3	4.7	0.6
Feb 2017	2.7	2.0	1.1	0.8
Mar 2017	1.4	0.9	3.9	0.4
Apr 2017	4.2	0.9	0.09	0.3

Appendix B – Daily weather statistics – June 2019

Date (June 2019)	Temp min (oC)	Temp max (oC)	Rain (mm)	Number of wet days (total)	Weather station - Hours recorded (n)	Avg wind speed (m/s)	Avg wind direction (deg)	Evapo transpiration (mm)
1	0.5	13.7	0.5		24.0	1.0	147.9	2.84
2	1.3	12.3	0.0		24.0	1.3	199.2	2.069
3	4.3	8.7	9.0		24.0	2.8	265.3	2.724
4	1.7	9.0	22.5		24.0	4.1	183.7	1.034
5	2.2	10.3	0.0		24.0	2.6	224.3	1.927
6	0.8	13.1	0.0		24.0	2.0	257.9	2.114
7	1.7	15.3	0.0		24.0	0.9	207.4	2.032
8	5.5	10.6	0.0		24.0	2.4	270.8	1.881
9	6.2	13.3	0.0		24.0	3.0	259.1	1.499
10	9.4	12.2	3.5		24.0	5.5	284.7	1.74
11	6.5	15.3	0.5		24.0	2.7	263.8	0.92
12	6.9	16.0	0.0		24.0	5.6	279.2	1.535
13	5.6	12.7	2.5		24.0	4.4	271.0	0.598
14	3.3	11.1	0.0		24.0	2.6	262.7	1.579
15	2.8	12.1	0.0		24.0	1.5	248.4	2.016
16	3.1	9.2	2.5		24.0	0.9	126.9	1.562
17	4.5	10.8	0.0		24.0	1.1	148.8	1.529
18	3.0	9.9	0.0		24.0	2.2	265.8	1.704
19	0.0	9.0	0.5		24.0	2.0	260.0	1.548
20	-2.4	8.2	0.0		24.0	1.0	211.8	1.475
21	-0.7	8.7	0.0		24.0	2.4	237.1	1.627
22	-0.9	10.1	0.0		24.0	1.6	191.2	2.258
23	-1.6	8.0	0.0		24.0	1.8	192.2	1.787
24	2.7	8.5	0.0		24.0	2.6	102.9	1.394
25	5.4	13.9	0.0		24.0	2.2	92.8	1.929
26	5.5	12.5	0.0		24.0	1.9	86.8	3.194
27	5.7	15.6	0.5		24.0	1.7	69.9	1.691
28	6.8	15.0	0.0		24.0	2.4	265.0	0.939
29	8.2	16.4	2.0		24.0	4.6	313.4	1.274
30	6.7	11.9	4.0		24.0	5.9	276.9	1.099
Average/Total	3.5	11.8	48	11		2.57		31.4
